

# Order Form

**ORDER** e: [roofsales@ultraframe.co.uk](mailto:roofsales@ultraframe.co.uk)

**QUOTE** e: [quotes@ultraframe.co.uk](mailto:quotes@ultraframe.co.uk)

ACCOUNT No

Company Name

Order Number

## JOB REFERENCE

Installer Company Name

Company Contact

Telephone No

Email

Delivery Address

## PLEASE SKETCH YOUR PREFERRED DESIGN HERE

- mark window, door & wall positions/types.

## INDICATE ON DRAWINGS IF ANY PART OF THE PROJECT IS EXISTING

### DIMENSIONS

Internal frame to internal frame

### ROOF U-VALUE:

0.15 (standard)

0.12 (thermally enhanced)

### PLAN VIEW

### POSTCODE

Delivery Date Req

Quotation Ref

### CRITICAL INFORMATION

\*Required for structural snow / wind loading

\*Site Postcode

Site Address\*\*

\*\*Required for any off mainland UK installations

Roof Pitch (°)

*CUSTOMER NOTE: Please carefully read the Ultrarroof Complete Guide to Selling, Surveying and Specifying before filling in order details.*

### HOW TO PLACE AN ORDER FOR ULTRAROOOF:

1. Sketch plan & elevations.  
(If necessary, attach photos of existing property. Indicate on drawings if any part of project is existing).
2. Mark and caption the positions of all walls, brick piers, windows/doors, cut outs / intrusions.
3. Mark the preferred positions of any
  - a) roof windows (vents) or velux
  - b) rectangular glazed panels.
4. Upon placement of your Ultrarroof order, an order confirmation is generated which must be signed and emailed back.

### NOTES:

Please see p29 of Ultrarroof guide to selling, surveying and specifying for list of what IS / IS NOT included

### FRONT ELEVATION

### LEFT ELEVATION

### RIGHT ELEVATION

Please sign and return to

[roofsales@ultraframe.co.uk](mailto:roofsales@ultraframe.co.uk) SIGNED

DATE

# Order Form

## JOB REFERENCE

|                                      |                                        |                                      |
|--------------------------------------|----------------------------------------|--------------------------------------|
| <b>ULTRAROOF TILE</b>                |                                        |                                      |
| <b>TILE COLOUR</b>                   |                                        |                                      |
| <input type="checkbox"/> Carbon grey | <input type="checkbox"/> Harvest brown | <input type="checkbox"/> Terra brick |
| <b>RIDGE / CAPS COLOUR</b>           |                                        |                                      |
| <input type="checkbox"/> Grey        | <input type="checkbox"/> Red           | <input type="checkbox"/> Brown       |

|                                   |                                      |                                      |
|-----------------------------------|--------------------------------------|--------------------------------------|
| <b>METROTILE</b>                  |                                      |                                      |
| <b>METROTILE COLOUR</b>           |                                      |                                      |
| <input type="checkbox"/> Charcoal | <input type="checkbox"/> Burnt umber | <input type="checkbox"/> Antique red |
| <b>RIDGE / CAPS COLOUR</b>        |                                      |                                      |
| <input type="checkbox"/> Grey     | <input type="checkbox"/> Red         | <input type="checkbox"/> Burnt umber |

## GUTTER

☐ White ☐ Black ☐ Grey ☐ Brown ☐ Caramel

## SOFFIT

☐ White ☐ Black ☐ Grey ☐ Rosewood ☐ Light Oak

## DOWNPIPE

☐ Round ☐ Square  
☐ White ☐ Black ☐ Grey ☐ Brown ☐ Caramel

## CORNICE (Curved ONLY)

☐ Yes ☐ Grey ☐ White

## FRAME STIFFENER (Always supplied\* on gable roofs, recommend on lean-to's above door sets - please confirm frame colour)

☐ Yes ☐ No ☐ Internal colour ☐ External colour

## STRUCTURAL GALLOWS BRACKET FOR BOX BEAM

(if design needs one, check survey guide)

☐ QTY .....

Soffit size (if there is one) .....

## GABLE BOLSTER

(If ticked, please confirm frame colour)

☐ To be specified if there are any doors in the gable.

## GLASS OPTIONS - WARM EDGE SPACER

### Super Energy Saving Glass

| Low Solar Gain                                    | Medium Solar Gain                                           | High Solar Gain                   |
|---------------------------------------------------|-------------------------------------------------------------|-----------------------------------|
| <input type="checkbox"/> Ultimate Blue<br>Aqua 4S | <input type="checkbox"/> Bronze 4S<br>Blue 4S<br>Neutral 4S | <input type="checkbox"/> Clear 4S |

### Good Thermal Efficiency

| Low Solar Gain                    | Medium Solar Gain                                              | High Solar Gain                    |
|-----------------------------------|----------------------------------------------------------------|------------------------------------|
| <input type="checkbox"/> Std Aqua | <input type="checkbox"/> Std Bronze<br>Std Blue<br>Std Neutral | <input type="checkbox"/> Std Clear |

## VELUX ROOF WINDOW (Velux windows not supplied. Velux products not included in price)

Please indicate positions on plan. NOTE: Ensure a Velux EDL flashing kit is ordered for each Velux window (not supplied).

☐ CK01 ☐ CK02 ☐ CK04 ☐ CK06

## ROOF VENTS AND MECHANISM (mark plan)

☐ Roof vent up to ridge ☐ Roof vent with glass above

Brass ☐ Manual Spindle ☐ Manual Spindle and pole ☐ Manual Spindle and telescopic pole  
Chrome ☐ Manual Spindle ☐ Manual Spindle and pole

☐ Electric motor with digital thermostat and rain sensor

☐ Electric motor and rocker switch

☐ Electric motor with radio and remote control

☐ Electric motor with thermostat (AVTD002)

☐ Electric without switch/thermostat (Motor only)

## ANCILLARY EXTRAS

The installer is responsible for ensuring that where Ultraroom is supported by means such as masonry or timber/ PVCu frame walls, the structure provides enough lateral support and resistance to wind uplift. Further guidance can be obtained through Ultraroom's technical documentation/ guides. Ultraframe is not responsible for the structural adequacy of any existing building work used as part of an overall project. Whilst assistance is provided ultimate responsibility for securing Building Regulations lies with the retail installer.

For further guidance please contact the Technical Support Team on  
01200 452918 or email [techsupport@ultraframe.co.uk](mailto:techsupport@ultraframe.co.uk)

Please sign and return to

[roofsales@ultraframe.co.uk](mailto:roofsales@ultraframe.co.uk)

SIGNED


DATE

# Order Form


JOB REFERENCE

## Ultrarroof on frames

**40mm soffit**




Brick & Block

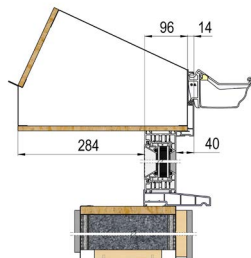


hup!

**151.5mm soffit**




Brick & Block

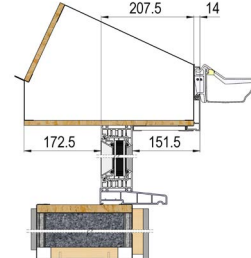


hup!

## Ultrarroof on walls

**72.5mm soffit**




Brick & Block




hup!

**Large soffits**




Brick & Block

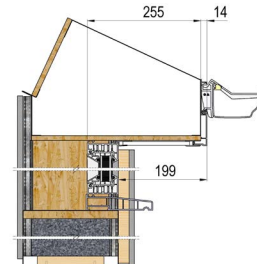


hup!

## Boundary wall options - Brick & block only

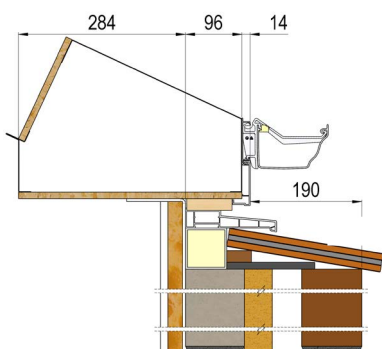

**-190mm soffit**

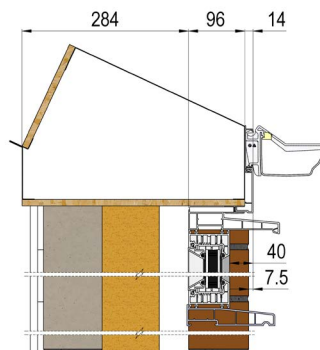

**0 soffits**

Please sign and return to

roofsales@ultraframe.co.uk

SIGNED

DATE

# Goalpost specification


**Goalpost Colour**

|                         |               |
|-------------------------|---------------|
| To match roof internals |               |
| Bespoke:- RAL colour    | Gloss Level % |

**Leg length**

|                         |                                                                                                      |
|-------------------------|------------------------------------------------------------------------------------------------------|
| Frame height            | NB. It is advised not to order any windows or doors until goalpost specification has been finalised. |
| Length below floor/cill |                                                                                                      |

**Goalpost leg example**

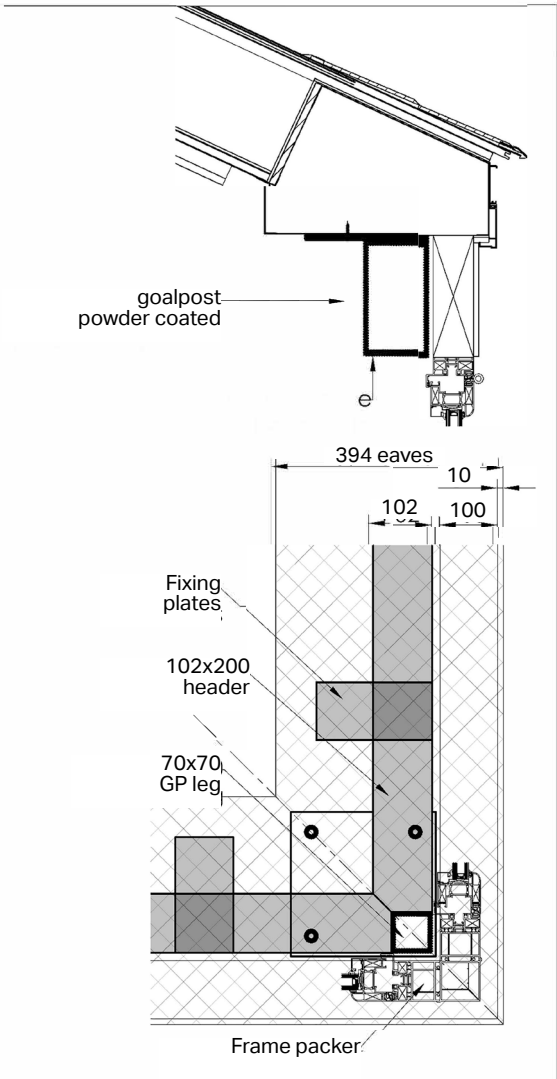

**Disclaimer:**

Ultraframe does not take responsibility for the structural stability of the entire structure, only the products provided by Ultraframe. To ensure the rest of the structure is suitable, it is the installers responsibility to ensure that all walls, foundations and building structure are compliant with Document A of Building Regulations. Any adjoining window frames must be a minimum of 70mm reinforced PVC frames, coupled in accordance with the manufacturer's recommendations. Host walls must be suitable to take the additional load and forces of the new building.

All beam end plates (WP and SP) must be bolted to a suitable substrate with adequate anchors. For the WP, the host wall suitability to accept the increased forces must be checked. The SP should be positioned on a suitable concrete padstone built into the supporting wall and strapped down to at least two additional courses.

Baseplates must be anchored using a minimum of 3no. M12 through bolts (minimum 6kN Tension/Uplift capacity per bolt). Foundations or floor slabs must be designed to accept the additional forces.
